

MEMORANDUM

Date: July 28, 2022

TO: Local Development Finance Authority Board (LDFA)

FROM: Tom Shewchuk, IT Director

CC: Marti Praschan, Chief Financial Officer

SUBJECT: Technology Park Project Status


As of July 1, 2022, the overall project is 29% complete, 54% of the conduit has been installed, and 61% of the vaults (handholes) installed. There are no major issues to report. Progress has stopped for the week of 7/18 due to the Ann Arbor Art Fair. Utility locating has been slow of late and has caused some delays.

Concrete restoration work is up to date. Concrete restoration cost was negotiated down to \$44.00 per square foot from \$55.00 a square foot. This resulted in a reduction in cost of approximately \$215,000.00.


We were able to utilize some existing city conduit for an approximate cost reduction of \$144,000.00. In addition, we were able to coordinate with a water main project currently in-progress on State St. and will realize additional savings.

Completion is still scheduled for Fall of 2022.

	Original Budget	Amount Expensed	Current Balance
Design and Engineering	\$334,550.00	\$334,550.00	\$0.00
Construction	\$4,099,286.72	\$1,952,708.15	\$2,056,578.57
Contingency	\$400,000.00	\$233,085.78	\$166,914.22

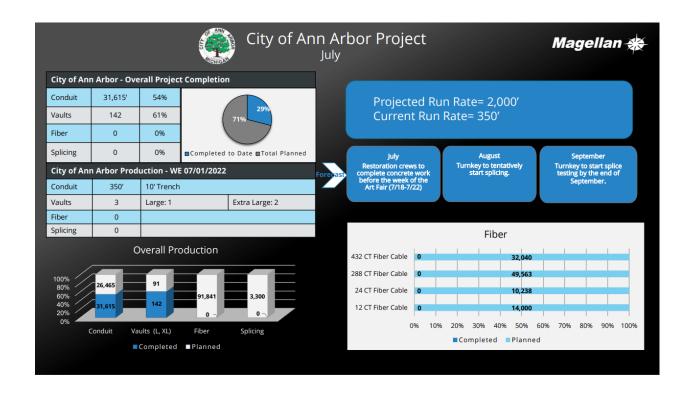

Progress Map as of 7/1/22

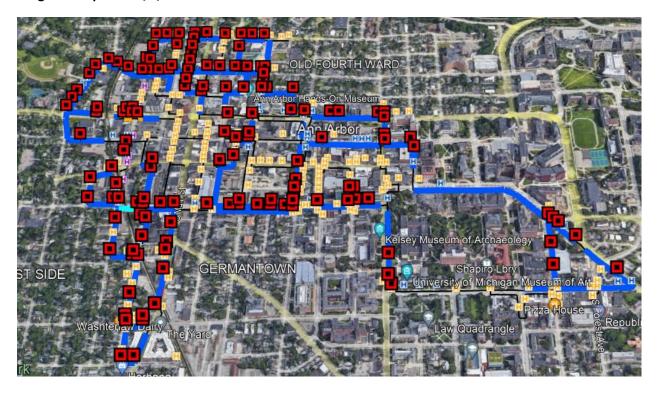

Please feel to contact me if you have any questions and thank you for your continued support.
